

Vacuum Charge Furnace PR-170029 — Final Hours Summary

Cenovus Lima, OH · Job USA26046 · WO 82036776 · Quotation DSP#26013 · 19 September 18:00 – 30 September 01:30, 2026 · 21 shifts · Service receipts 7077–7100

QUOTED 134 hours	FINAL 247.5 hours, incl. 52 stand-by	VARIANCE +113.5 hours, +85%	PASSES COMPLETED 8 of 8 decoked and inspected
-------------------------------	---	--	--

Scope completed

- All eight passes decoked through the convection and all five radiant segments, 3,595 ft of convection and 3,459 ft of radiant tube.
- Clean IDs confirmed by field measurement at 4.0", 3.8", 5.7", 7.8", 9.75" and 11.75", matching the coil drawings.
- All eight passes smart pigged. Pass 1–3 data approved 25 September; passes 4 and 6 on 26 September; passes 5, 7 and 8 completed 28 September.
- Filtration run throughout on filter press 1.
- Heater dewatered, launchers and hoses removed, filter presses cleaned at the wash pad, and equipment demobilised from the unit.

Pumping unit, by task


TASK	QUOTED HRS	ACTUAL HRS	Δ HRS	DETAIL
Rig-in	6	14	+8	Rig-in could not be completed in a single pass. It was worked in four separate periods of 5, 2, 4 and 3 hours as access to the launcher connections allowed, each restart carrying its own set-up.
Pigging	66	63	−3	All eight passes decoked within the quoted allowance. The coil cleaned to size on the planned progression, with minimal deposit found in the larger radiant bores.
Smart pig support	38	74	+36	Pumping unit time supporting the inspection contractor. Inspection was accepted section by section rather than by complete pass, so passes were re-entered to collect the outstanding diameters. The 4", 6" and 8" sections each required repeat runs; the field record of 24 September notes data loss on pass 3 and on the 4" of passes 1 and 2.
Rig-over	18	8	−10	Two rig-overs were required rather than the phased moves the quotation assumed, saving ten hours against plan.
Rig-out	6	36.5	+30.5	Dewatering of all eight passes, removal of the 6" and 12" launchers and hoses, the filter press dropped and cleaned at the wash pad, pigs and crates loaded, and equipment demobilised from the unit and the facility. The final shift ran 18:00 to 01:30 on 29–30 September; all units are recorded to that finish, not a full shift.
Productive total	134	195.5	+61.5	

Equipment

LINE	QUOTED HRS	ACTUAL HRS	Δ HRS	DETAIL
Support trailer 6	134	240.5	+106.5	On site from 01:00 on 20 September through demobilisation.
Filter press 1	134	235.5	+101.5	Filtration ran for the full duration of the job.
Crew trucks	134	244.5	+110.5	One crew truck per shift across a 21-shift job.

Vacuum Heater Timeline

Task hours for each of the 21 shifts, by service receipt, as recorded on the dated field tickets.

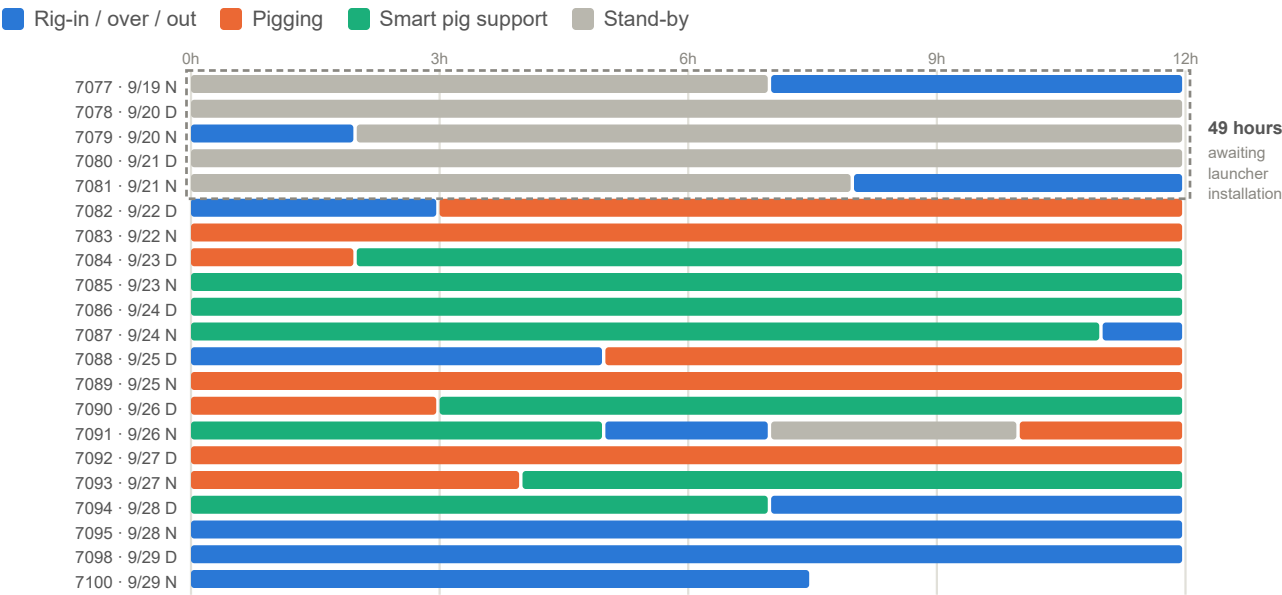

Stand-by

Fifty-two hours were booked to stand-by, a category the quotation carries no allowance for. Every one of those hours is recorded on a dated field ticket as waiting on the **12" radiant-outlet launchers to be installed by facility pipefitters**. Forty-nine were spent before the launchers were first hung on the night of 21 September, and a further three on 26 September waiting for them to be moved to passes 5, 7 and 8. The requirement is named on every ticket across that run.

PERIOD	HOURS	DETAIL
19–21 September	49	Pumping unit and crew on site and available. Convection launchers and hoses were connected during this period as access allowed; the coil could not be entered until the radiant-outlet launchers were in place.
26 September	3	Waiting for the 12" launchers to be relocated to passes 5, 7 and 8 before the final three passes could be filled.
Stand-by total	52	

Prepared from daily service receipts 7077–7100. Every hour shown is as recorded on a dated field ticket; no figure is estimated or allocated across tasks. USA DeBusk, LLC.
