Vacuum Charge Furnace PR-170029 — Change Order Summary

Cenovus Lima, OH · Job USA26046 · WO 82036776 · Quotation DSP#26013 · 19 September 18:00 – 30 September 01:30, 2026 · 21 shifts · Service receipts 7077–7100

CO-1 STAND-BY	CO-2 SMART PIGGING	DECOKING TIME SAVED	NET CHANGE
$54,491.84	**$37,725.12**	**−$13,622.96**	**$78,594.00**
52 hours	36 hours over quote	13 hours under quote	change orders less savings

Rates. Equipment **$800.00 per hour** ($19,200 per 24 hours). Personnel **$210.42 per hour** ($2,525.00 per 12-hour shift). Per diem **$450.00 per shift**, charged on each 12 hours of change-order time. Hours are as recorded on the signed daily service receipts.

CO-1 — Stand-by

Fifty-two hours of stand-by are recorded on the signed tickets, a category the quotation carries no allowance for. The crew and pumping unit were on site and available throughout. Every hour is recorded as waiting on facility work: the pumping unit being spotted in the unit, then the **12" radiant-outlet launchers being installed by facility pipefitters**, and later relocated to passes 5, 7 and 8.

RECEIPT	SHIFT	HOURS	RECORDED CAUSE
7077	19 Sep night	7	Waiting on the pumping unit to be spotted in the unit
7078	20 Sep day	12	12" radiant-outlet launchers not yet installed
7079	20 Sep night	10	12" radiant-outlet launchers not yet installed
7080	21 Sep day	12	Waiting for pipefitters to install the 12" launchers
7081	21 Sep night	8	Waiting on the 12" launchers, installed 02:00
7091	26 Sep night	3	Waiting for pipefitters to move the 12" launchers to passes 5, 7 and 8
Total		**52**	

LINE	HOURS	RATE	AMOUNT
Equipment	52	$800.00	$41,600.00
Personnel	52	$210.42	$10,941.84
Per diem (4.33 shifts)	52	$450.00 / shift	$1,950.00
CO-1 total	**52**		**$54,491.84**

CO-2 — Smart pigging

The quotation allowed 38 hours of pumping-unit support for the inspection contractor; 74 hours were required. Inspection was accepted section by section rather than by complete pass, so passes were re-entered to collect the outstanding diameters. The 4", 6" and 8" sections each required repeat runs, and the 24 September ticket records data loss on pass 3 and on the 4" of passes 1 and 2.

LINE	HOURS	RATE	AMOUNT
Equipment	36	$800.00	$28,800.00
Personnel	36	$210.42	$7,575.12
Per diem (3 shifts)	36	$450.00 / shift	$1,350.00
CO-2 total	**36**		**$37,725.12**

Decoking time saved


All eight passes were decoked inside the quoted allowance, and two rig-overs replaced the phased moves the quotation assumed.

TASK	QUOTED HRS	ACTUAL HRS	SAVED HRS	EQUIPMENT	PERSONNEL	PER DIEM	SAVED
Pigging	66	63	3	$2,400.00	$631.26	$112.50	$3,143.76
Rig-over	18	8	10	$8,000.00	$2,104.20	$375.00	$10,479.20
Total	**84**	**71**	**13**	**$10,400.00**	**$2,735.46**	**$487.50**	**$13,622.96**

Summary

CO-1 Stand-by, 52 hours	$54,491.84
CO-2 Smart pigging, 36 hours over quote	$37,725.12
Change orders total	**$92,216.96**
Decoking time saved, 13 hours under quote	−$13,622.96
Net change	**$78,594.00**

Shift timeline

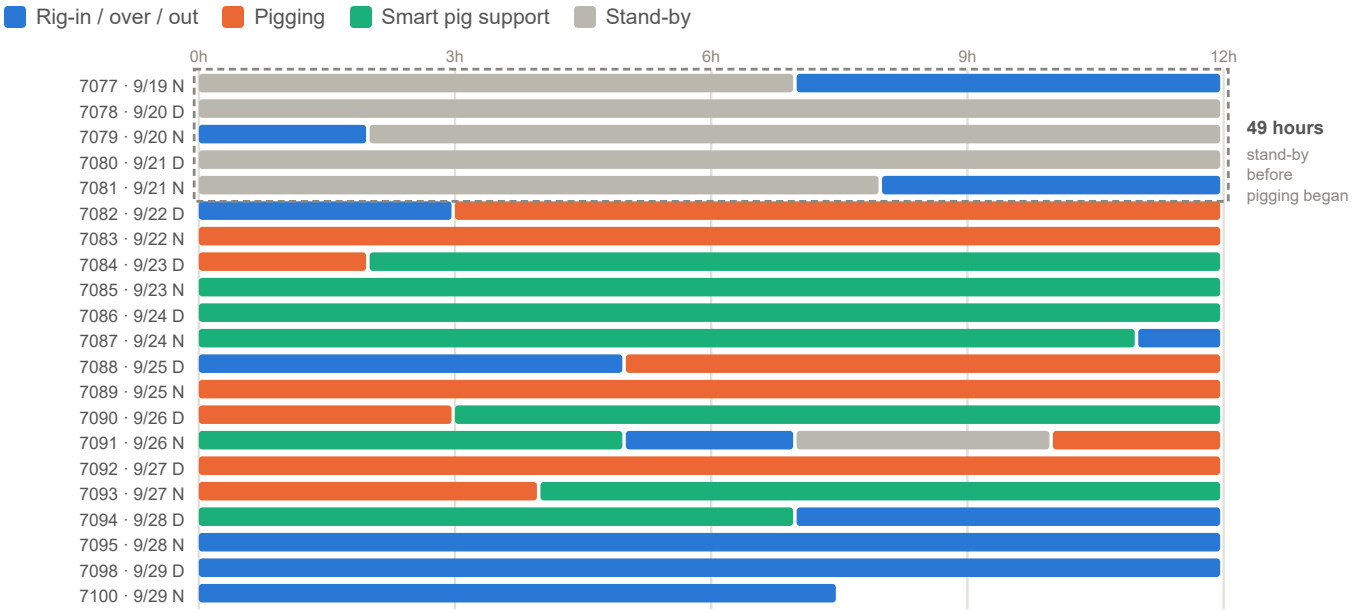

Prepared from signed daily service receipts 7077–7100. Every hour shown is as recorded on a dated field ticket. USA DeBusk, LLC.
